

INVESTOR PROGRESS UPDATE JUNE 2020





MILESTONES OF THE MONTH

01

Construction of Awali
Estate Ongoing

02

Construction of
1255-Palm Ridge Ongoing

03

Construction of Vipingo
Leisure Centre Ongoing

04

Installation of Sea Water
Desalination Plant Ongoing



Creating a Promising Future



AWALI

ESTATE





PROJECT FACT SHEET

AWALI ESTATE PROJECT PROGRESS FACT SHEET


No of units	74
Construction duration	85 Weeks
Construction duration to date	78 Weeks
Construction duration to completion	7 Weeks
Progress status	ON SCHEDULE
Show Houses	Complete

JUNE ACTIVITIES

Batch 1	Tiling Complete; Painting Complete
Batch 2	Tiling Complete; Painting Complete
Batch 3	Tiling Complete; Painting Complete
Batch 4	Painting and Tiling Ongoing
Batch 5	Painting, Tiling and Landscaping Ongoing

AMENITIES AND UTILITIES PROGRESS

COMPONENT	STATUS	TARGET COMPLETION DATE
Children's play area	Complete	Complete
Perimeter fence	Complete	Complete
CCT	Complete	Complete
INFRASTRUCTURE		
Roads	Ongoing	July 2020
Permanent power connection	Complete	Complete
Gate house	Complete	Complete
ICT	Ongoing	July 2020
LANDSCAPING		
Grassing	Ongoing	June 2020
Trees and Flowers	Ongoing	June 2020

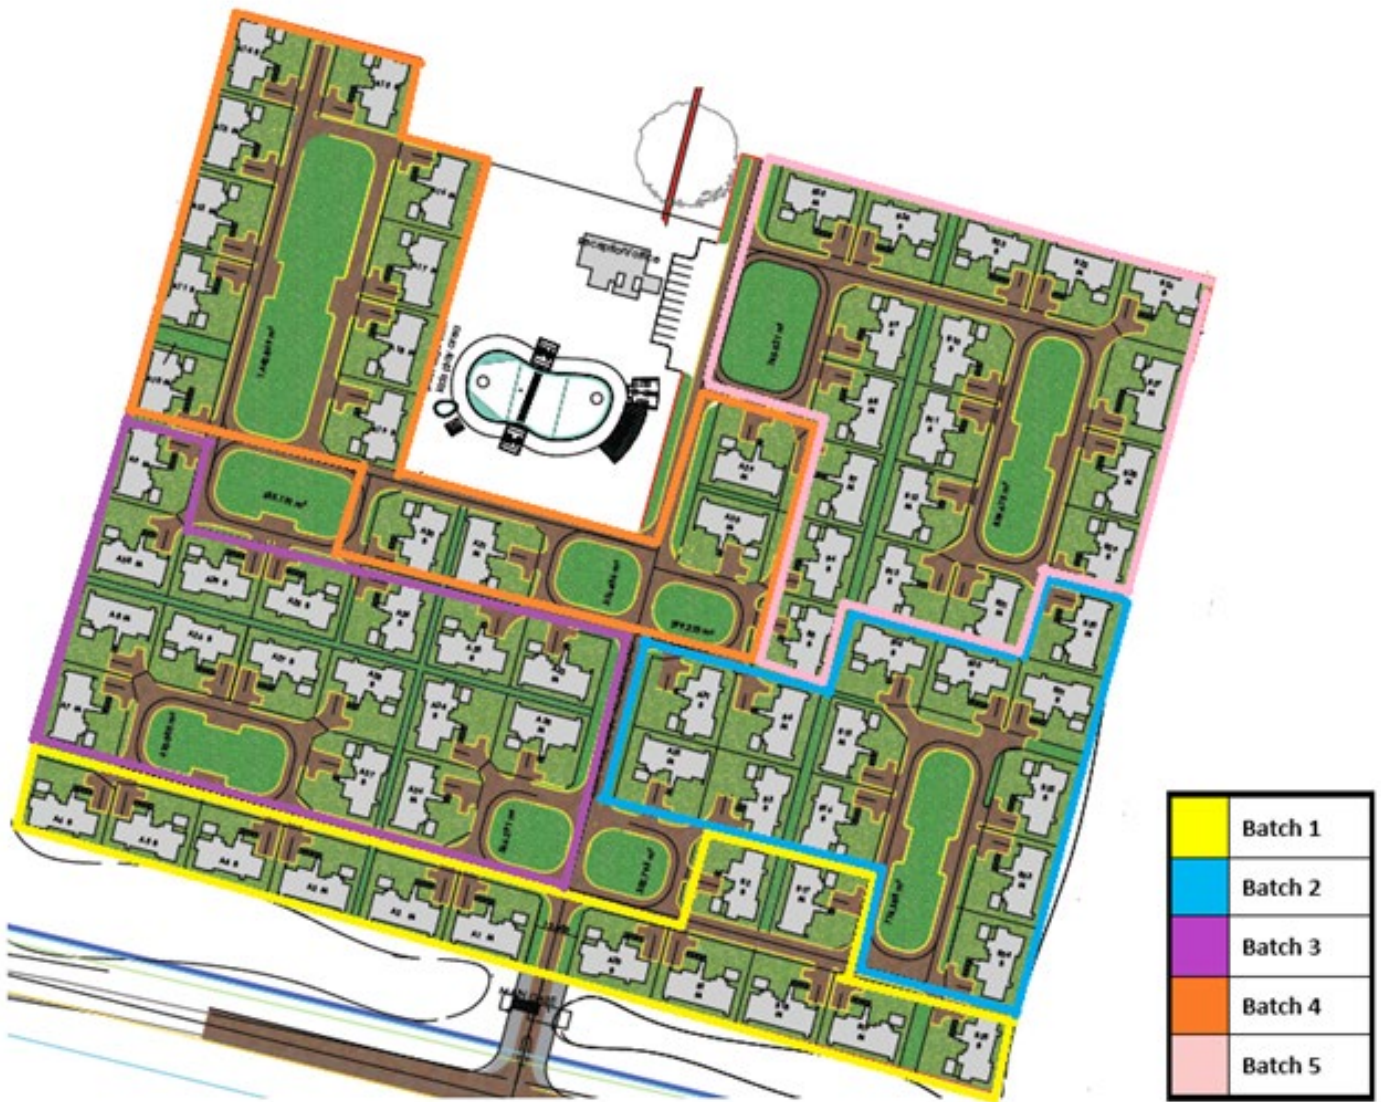

AWALI SITE OVERVIEW

The site map shows the 74 units and the construction progress.

- Batch 1: Tiling Complete; Painting Complete
- Batch 2: Tiling Complete; Painting Complete.
- Batch 3: Tiling Complete; Painting Complete
- Batch 4: Painting and Tiling Ongoing
- Batch 5: Painting, Tiling and Landscaping Ongoing

CONSTRUCTION PROGRESS UPDATE PHOTOS

Batch 1



Batch 2



Batch 3




Batch 4



Batch 5



1255 PALM RIDGE

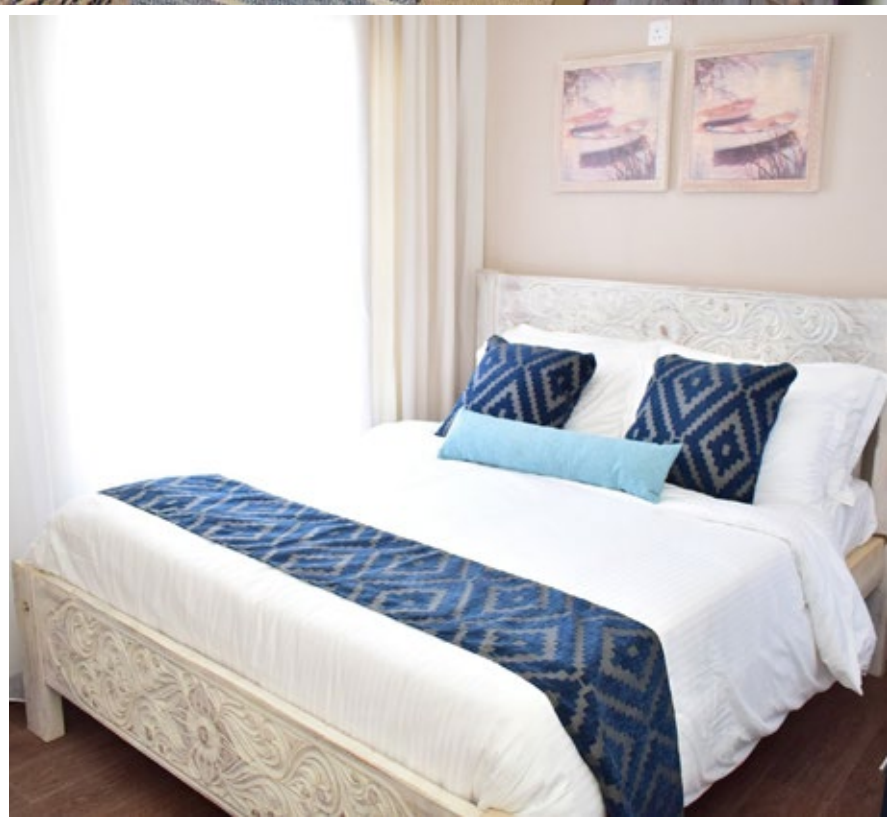



PROJECT FACT SHEET

1255-PALM RIDGE PROJECT PROGRESS FACT SHEET

No of units	330 (Phase 1)
Construction duration	90 Weeks
Construction duration to date	68 Weeks
Construction duration to completion	22 Weeks
Progress status	ON SCHEDULE
Show Houses	Ongoing
JUNE ACTIVITIES	
PHASE 1	
Block A1	Window Fixing, Painting and Tiling Ongoing
Block B1	Window Fixing, Painting and Tiling Ongoing
Block C1	Window Fixing, Painting and Tiling Ongoing
Block A2	Plastering Complete
Block B2	Plastering 90% Complete
Block C2	Roofing Ongoing
Block A3	Third Floor Walling Ongoing
Block B3	Fourth Floor Walling Ongoing
Block C3	Roofing and Painting Ongoing
PHASE 2	
Block D1	Foundation excavation complete
Block D2	Foundation Walling ongoing
Block D3	Foundation Walling complete

AMENITIES AND UTILITIES PROGRESS

COMPONENT	STATUS	TARGET COMPLETION DATE
Swimming pool	Scheduled	November 2020
Children's play area	Scheduled	October 2020
Parks	Scheduled	October 2020
Perimeter fence	Scheduled	October 2020
INFRASTRUCTURE		
Roads	Ongoing	October 2020
Permanent power connection	Complete	Complete
Gate house	Ongoing	August 2020
ICT	Scheduled	October 2020
LANDSCAPING		
Grassing	Scheduled	October 2020
Trees and Flowers	Scheduled	October 2020

CONSTRUCTION PROGRESS UPDATE PHOTOS





Phase 2



Phase 2



Phase 2



Phase 2



**...a little progress
each day adds up
to big results....**

KINGSWOOD PARK

Own Land at Kenya's most exquisite address and get to build your dream home. Buy an 1/8th Acre plot at KES 2.5 Million and enjoy a flexible payment plan.



KINGSWOOD MIRABELLA



KINGSWOOD MAISONETTE



KINGSWOOD BUNGALOW



KINGSWOOD RIVIERA



VIPINGO SEA WATER DESALINATION PLANT

Installation of the 3 million litre sea water desalination plant is currently ongoing.



SAND FILTERS & WATER TANKS



3 MILLION
LITRES
WATER TANK

ELECTRICAL CONTROL ROOM



VIPINGO DEVELOPMENT LIMITED

1st Floor, Vipingo Ridge Conference Centre
P. O. Box 117 – 80119 Vipingo

Website: www.vipingodevelopment.com

Email: info@vipingodevelopment.com

Mobile: +254 740 400 215

Tel: +254 4400 215

WE ARE ON SOCIAL MEDIA



Vipingo Development LTD



@VipingoLTD



Vipingodevelopmentlimited



Vipingo Development

