

August 2026

NEWSLETTER

TRANSFORMING VISION INTO THRIVING COMMUNITIES



Nairobi Office

+254 747 01 99 77
sales@tworivers.co.ke

Vipingo Office

+254 747 01 99 78
info@vipingodevelopment.com

Entebbe Office

+256 707 76 40 20
sales@pearlmarina.co.ug



TABLE OF CONTENTS

03

● **LETTER FROM THE MD**

A personal note from our Managing Director

05

● **NAIROBI PROJECT UPDATES**

Stay informed on the progress, milestones and future plans for our Nairobi-based projects.

25

● **A FASTER WAY TO BUILD**

-An article by Ednah Mwendwa

35

● **VIPINGO PROJECT UPDATES**

Stay informed on the progress, milestones and future plans for our Vipingo Development projects.

55

● **AUGUST EVENTS GALLERY**

We invite you to explore the stories that defined the month and the activities we have held.

FROM THE MANAGING DIRECTOR

Dear Esteemed Clients,
I hope this message finds you well.

It is always encouraging to reflect on how far we have come and, more importantly, to see the vision we shared with you steadily taking shape. Every milestone achieved is a reminder that we are not simply developing properties; we are creating places that you will be proud to call home.

I am pleased to share that we continue to make strong and steady progress across our developments, with significant milestones being achieved across our various projects. Our teams remain focused on maintaining momentum, ensuring that each phase progresses efficiently and to the high standards we have set. The transformation taking place across our developments is a testament to the commitment of our teams and partners, and we are encouraged by the progress being made towards delivering on our commitments to you.

We recognise that these developments represent an important investment in your future, and we deeply value the trust you have placed in us. We remain committed to honouring that trust through quality, timely execution and thoughtful development. With every milestone, we move closer to delivering spaces that meet your expectations, create lasting value and contribute meaningfully to the communities we are building.

Thank you for your patience, trust and continued confidence in us. We look forward to sharing more milestones with you in the months ahead and, ultimately, to welcoming you home.

Warm regards,



KENNETH MBAE
CENTUM REAL ESTATE



INTRODUCING A NEW INVESTMENT OPPORTUNITY AT VIPINGO



SEA 'N' SISAL

An exclusive coastal community where understated luxury comes together in perfect harmony, offering stunning sunrises over the Indian Ocean and beautiful sunsets across the hills.

¼ ACRE	7,500,000
½ ACRE	14,000,000
¾ ACRE	21,000,000
1 ACRE	28,000,000

NAIROBI PROJECTS



From vibrant mixed-use communities to thoughtfully designed residential developments, our Nairobi projects continue to shape the way people **live, work and connect**.

Take a look at our latest project progress and see how these developments are taking shape, one milestone at a time.

+254 747 019 977
sales@tworivers.co.ke

We are here to keep you informed every step of the way.



RIVERBANK II APARTMENTS

Welcome to the recent update for Riverbank II Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.




HIGHLIGHTS

Following the recent groundbreaking of Riverbank II, we have made impressive progress into active construction. Works on site have advanced steadily, with key early construction activities already underway.

Stripping and excavation works have been ongoing, being the preliminary steps of foundation works.

September Targets



Activity	September Targets
Stripping and excavation for foundation.	90%
Drilling & concreting of piles (foundation works).	10%

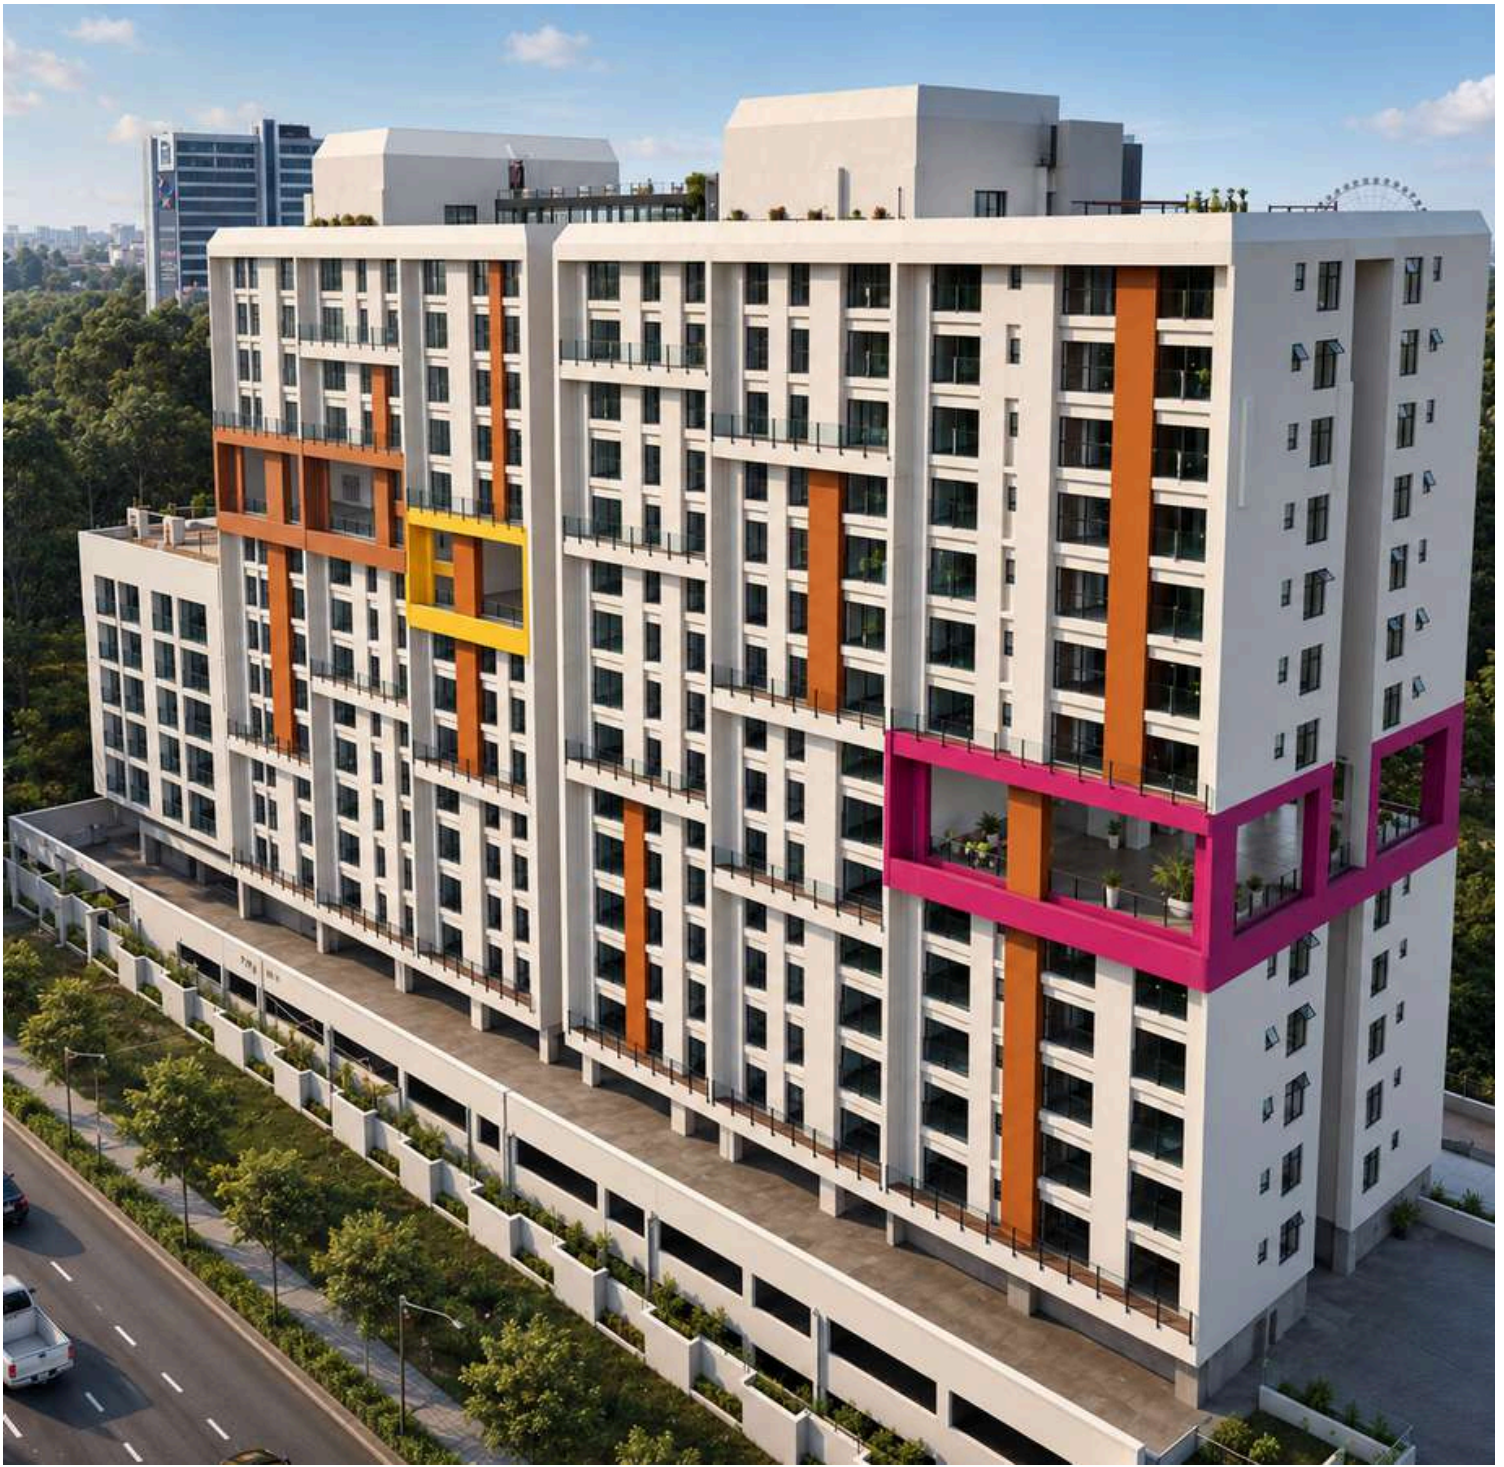

CASCADIA APARTMENTS

Welcome to the recent update for Cascadia Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.

OVERVIEW

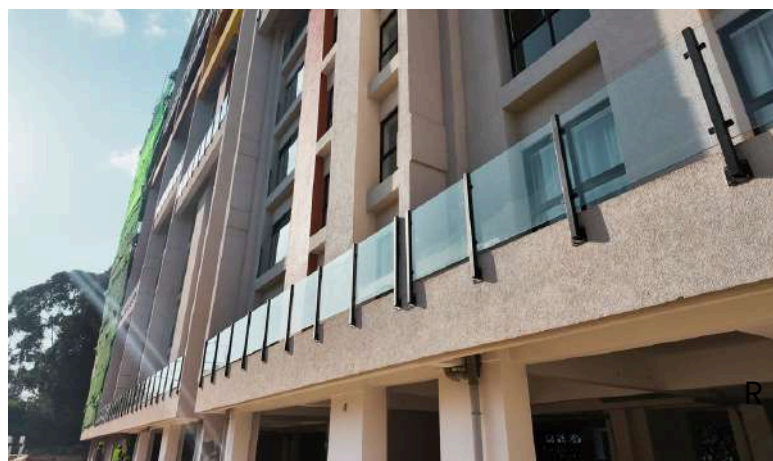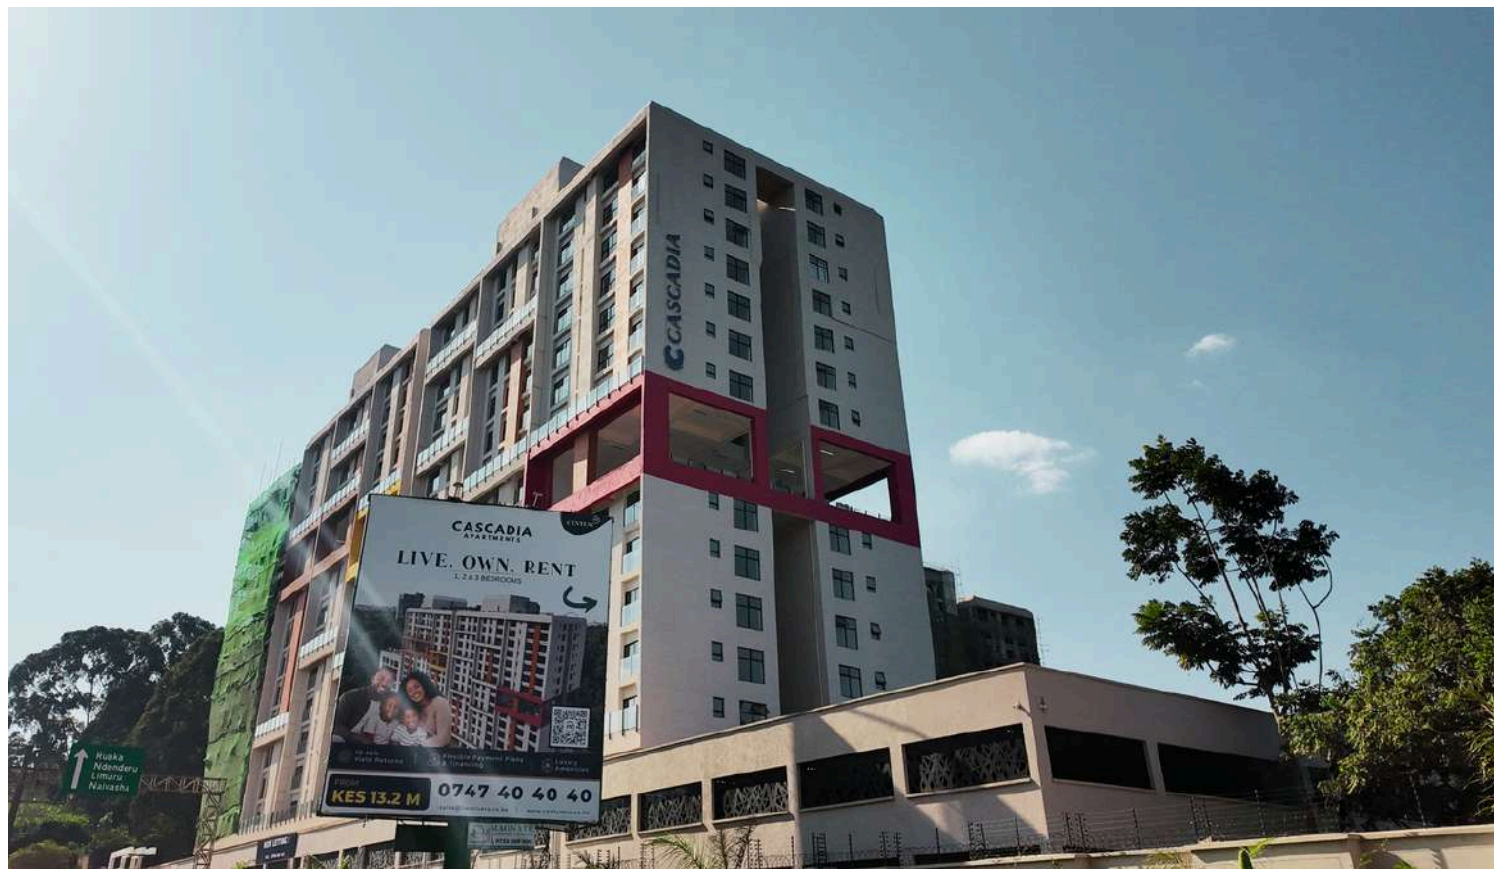

The project is progressing well, with noticeable improvements across the site. In particular, Block C has made significant progress, having previously been slightly behind schedule, and is now showing encouraging momentum towards catching up with the other blocks.



August Activities & Progress Achieved

Over the past month, the project has made remarkable progress, bringing the vision closer to reality. Every milestone achieved reflects our commitment to quality and exceptional living.

Here is a breakdown of the targets that had been set for the month and the progress achieved.

Block D

Activity	August Targets	Progress Achieved
Snagging Units	100%	99%
Snagging Common areas	100%	99%
Handing over inspections	70%	70%

Block E

Activity	August Targets	Progress Achieved
Snagging Units	100%	99%
Snagging Common areas	100%	99%
Testing and commissioning Lifts	70%	70%

External Works

Activity	August Targets	Progress Achieved
River Training and Protection	80%	82%
Retaining wall along Block A,B and C	45%	45%
Bridge works	30%	35%

Block A

Activity	August Targets	Progress Achieved
Internal masonry works	100%	95%
Electrical First fix	100%	95%
Plumbing First fix	100%	95%
Internal plasterwork	100%	95%
External plasterworks	100%	95%
Internal floor tiling	100%	15%

Block B

Activity	August Targets	Progress Achieved
Internal wall skimming	100%	95%
Internal floor tiles	100%	95%
External aluminium window frames	100%	95%
Internal door leafs	100%	85%
Internal wall tiling	50%	50%
Internal Joinery works	20%	15%

Block C

Activity	August Targets	Progress Achieved
Level 1 to 8 Masonry works	100%	60%
Level 13 slab	100%	100%
Level 13 to 14 Columns RC	100%	100%
Level 1 to 8 Limuru road plasterworks	100%	60%

BLOCK D & E



HIGHLIGHTS

With residents already moving in, the two blocks have already come to life, with homeowners settling into their new spaces and enjoying the comfort, quality and overall living experience that Cascadia offers.




BLOCK A



HIGHLIGHTS

Interior plastering, tiling, and door frame installation are ongoing, marking steady progress towards the completion of the internal works and bringing the spaces closer to their finished state.

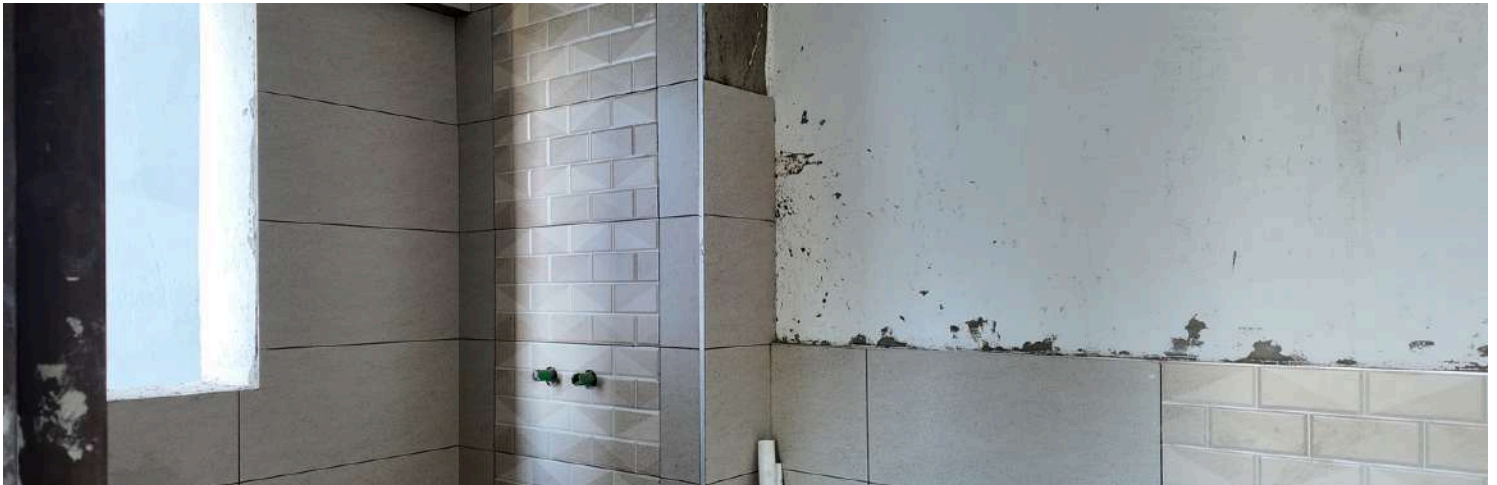

BLOCK B



HIGHLIGHTS

Key finishing and installation works are advancing steadily. External undercoat application is done, while interior works are taking shape through tiling, doors installation and electrical wiring.



BLOCK C



HIGHLIGHTS

Block C has recorded a significant achievement, reaching the 14th slab level, marking substantial progress in the structural works.

Masonry works are ongoing alongside electrical and mechanical installations, demonstrating continued advancement across multiple stages of construction.



September Targets

Looking ahead to September, our focus shifts to completing outstanding tasks from August and initiating the next activities for the Cascadia Apartments project.

The following table outlines our key activities and targets for the upcoming month.

Block D

Activity	September Targets
Snagging Units	100%
Snagging Common areas	100%
Handing over inspections	85%

Block E

Activity	September Targets
Snagging Units	100%
Snagging Common areas	100%
Testing and commissioning Lifts	85%

External Works	September Targets
River Training and Protection	85%
Retaining wall along Block A,B and C	45%
Bridge works	40%

Block A


Activity	September Targets
Internal masonry works	100%
Electrical First fix	100%
Plumbing First fix	100%
Internal plasterwork	100%
External plasterworks	100%
Internal floor tiling	100%

Block B

Activity	September Targets
Internal wall skimming	100%
Internal floor tiles	100%
External aluminium window frames	100%
Internal door leafs	100%
Internal wall tiling	70%
Internal Joinery works	50%

Block C

Activity	September Targets
Level 1 to 12 Masonry work	100%
Level 1 to 8 Limuru road plasterworks	100%
Level 14 Slab	100%
Level 14 to 15 Columns RC	100%



26 MZIZI COURT

Welcome to the recent update for 26 Mzizi Court Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.

PHASE 1

August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Block B

Activity	August Targets	Progress Achieved
Internal plasterworks level 16 - 17.	100%	99%
External aluminium windows - All façades	100%	95%
Internal skimming at level 2-17	100%	99%
Interior undercoat painting on levels 12 - 15.	100%	99%
Wardrobe & Kitchen cabinet fitting on levels 6 - 13.	100%	95%
Tiling of wet areas at level 8 - 9.	100%	100%
Fixing of Kitchen wall tiles at levels 3 - 7.	100%	100%

Block C

Activity	August Targets	Progress Achieved
Walling at level 16 - 17.	100%	85%
Aluminium window frames installation	100%	75%
Floor screeding on levels 5 - 8.	100%	99%
Internal plaster on levels 13 - 15.	100%	98%
Internal skimming on levels 5 - 7.	100%	50%
Installation of common area staircases railing.	100%	95%

Block B & C



Site Overview

BLOCK B



HIGHLIGHTS

The installation of kitchen cabinetry, countertops, wardrobes, tiling and electrical fittings is giving the apartments its final look and feel.


With these finishing works well underway, the project is steadily approaching the final stages of completion and will soon be ready for residence.



BLOCK C



Key works including internal finishes, tiling, electrical installations and joinery are steadily taking shape, giving the spaces a clearer sense of their final form.

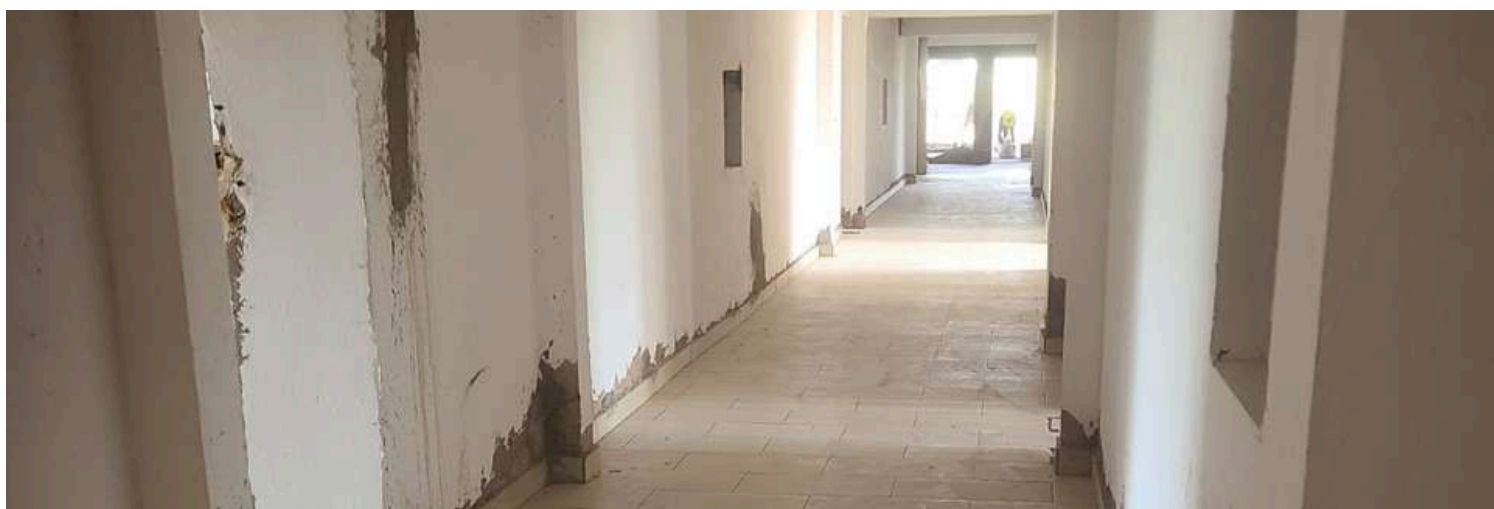

September Targets

Looking ahead to September, our focus shifts to completing outstanding tasks from August and initiating the next activities for the 26 Mzizi Court Apartments project.

The following table outlines our key activities and targets for the upcoming month.

Block C

Activity	September Targets
Walling at level 16 - 17.	100%
Aluminium window frames installation	100%
Floor screeding on levels 5 - 8.	100%
Internal plaster on levels 13 - 15.	100%
Internal skimming on levels 5 - 7.	100%
Installation of common area staircases railing.	100%

Block B

Activity	September Targets
Internal plasterworks level 16 - 17.	100%
External aluminium windows - All façades	100%
Internal skimming at level 2-17	100%
Interior undercoat painting on levels 12 - 15.	100%
Wardrobe & Kitchen cabinet fitting on levels 6 - 13.	100%
External painting.	100%
Installation of doors at levels 13 - 17.	100%

PHASE 2



Block D

Activity	August Targets	Progress Achieved
Drilling & concreting of piles (foundation works).	100%	84%

September Targets

Activity	September Targets
Drilling & concreting of piles (foundation works).	100%

Block E

Activity	August Targets	Progress Achieved
Piles trimming (foundation works).	100%	100%
Pile cap excavation (foundation works).	100%	100%

September Targets

Activity	September Targets
Formwork & reinforcement of pile cap.	50%

A Faster, Smarter Way to Build: Aluminium Formwork at 26 Mzizi Court.

Something different is about to take shape at 26 Mzizi Court. Blocks D, E and F will be constructed using aluminium formwork, a building system that allows walls and floor slabs to be cast together with greater speed, precision and consistency. Before the first panel goes up, here is a closer look at how the system works, why it has been adopted at Mzizi, and what it means for your future home.

Why Change How We Build?

Most buildings you see going up around Nairobi today typically follow the same method: a reinforced concrete frame is cast first, then concrete block walls are laid in, and finally everything is plastered smoothly by hand. While this conventional approach works, it involves several sequential construction activities that can affect the pace of delivery, and with Kenya's housing shortage, demand for new homes far outpaces what the industry delivers each year. This means people need faster ways to build without giving up quality.

Aluminium formwork offers a more integrated approach. It is a construction technology that has been adopted internationally and is increasingly being used by developers locally to improve construction efficiency while maintaining the required structural and quality standards. This is why it has been selected for Blocks D, E and F at Mzizi.

What exactly is Aluminium formwork?

Instead of building a frame first and filling in walls afterward, aluminium formwork allows walls, columns where applicable, beams, and floor slabs to be formed and cast as part of the same construction cycle. Precision-engineered aluminium panels are locked together on site to form a complete mould for an entire floor.

Reinforcement, electrical conduits, and plumbing provisions are incorporated before concrete is poured into the formwork. Once the concrete has achieved the required strength, the walls and floor come out as a single, seamless, monolithic structure. The panels are then unclipped, cleaned, and lifted to the next floor for reuse.



How It Comes Together on Site

1. **Site readiness** – Reinforcement, electrical conduits and plumbing sleeves for the first level are completed and checked against the structural drawings. Reference lines are then marked out to ensure that the formwork is positioned accurately.
2. **Panel erection** – Corner panels go up first, followed by wall panels, slab corners, beams, and finally the slab panels. Wedge pins and flat ties connect the panels to create a rigid and stable formwork system ready for the concrete pour.
3. **Concrete pour** – Concrete is poured uniformly and vibrated to eliminate air pockets, producing walls and slabs in one continuous, monolithic pour.

4. **Curing, dismantling and reuse** – Once the concrete reaches the required strength, panels are carefully removed, cleaned, and moved up to the next floor, ready to be reused.

Because the same panels are reused floor after floor, once the cycle gets going, each level will go up in a matter of weeks rather than the months a blockwork floor typically takes.



Why This Matters for You

- **Stronger, safer homes** - Casting walls and slabs together creates a continuous reinforced-concrete structure designed to provide a robust and durable building system.
- **A smoother finish** - The precision of the aluminium panels produces straight, consistent concrete surfaces, which can reduce the need for extensive plastering and contribute to cleaner architectural finishes.
- **Faster delivery** - Reusable panels and a standardized process mean floors come up far quicker than conventional construction, translating to an earlier move-in date.
- **Precision and Consistency** - Every unit on every floor is dimensionally identical, so what you see on one floor is exactly what you will see on the other.

The Environmental Case

Aluminium panels are engineered for hundreds of reuses, which sharply cuts down on construction waste over the life of a project. Skipping the plastering stage also reduces the amount of cement, sand, and water used purely for finishing. And at the end of its working life, the aluminium itself is fully recyclable, rather than ending up in a landfill.

What's Next?

With the formwork now on site and preparation underway, the first panels are expected to go up soon.

For Blocks D, E, and F, this marks the beginning of a new construction phase, one where technology, precision and efficiency come together to shape the next generation of homes at 26 Mzizi Court.

Have questions about the construction process at Mzizi Court? Reach out to our team, and we would be happy to take you behind the scenes and tell you more about how your future home is taking shape.

-An Article by Ednah Mwendwa, Centum Real Estate



265 ELMER ONE

Welcome to the recent update for 265 Elmer One Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.

August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Block C

Activity	August Targets	Progress Achieved
Lift electrical works and signalization	30%	10%
Staircase railing	50%	10%
External Undercoat paint	100%	95%
Floor screed level 1,2,3,4	100%	10%
Aluminium windows installation level 3 to 8	100%	85%
Sewerline connection	100%	30%
KPLC Power connection	40%	10%
Electical works	20%	10%

Block B

Activity	August Targets	Progress Achieved
Floor screed level 1 to 6	50%	0%
Aluminium windows installation level 1 to 8	50%	0%

Block A

Activity	August Targets	Progress Achieved
External Undercoat paint -rear elevation	80%	45%
Lift electrical works and signalization	100%	30%
Internal plaster level 6 to 7	100%	70%
Complete power house	100%	60%
Convenience store	100%	0%
Boundary wall	60%	40%
Aluminium windows installation level 1 to 4	60%	30%




September Targets

Looking ahead to the new month, our focus shifts to completing outstanding tasks from August and initiating the next activities for the 265 Elmer One Apartments project.

The following table outlines our key activities and targets for the upcoming month.

Block C

Activity	September Targets
Lift electrical works and signalization	30%
Staircase railing	60%
External Undercoat paint	100%
Floor screed level 1,2,3,4	100%
Aluminium windows installation level 3 to 8	100%
Sewerline connection	100%
KPLC Power connection	40%
Electical works	20%

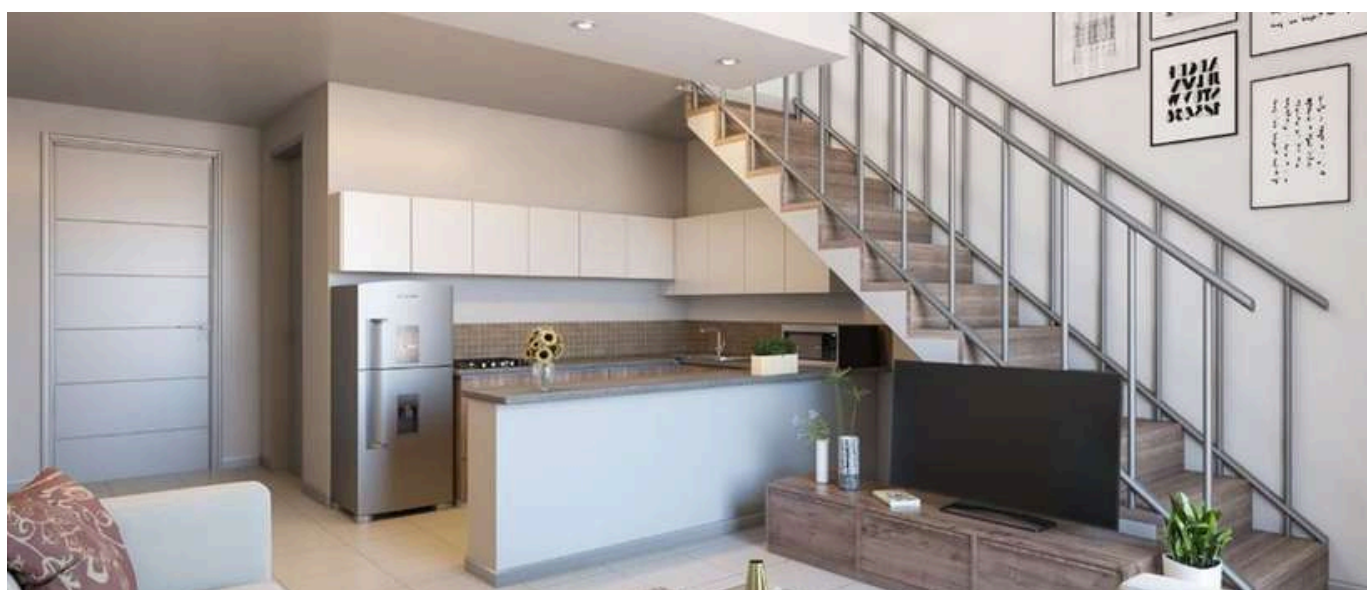

Block B

Activity	September Targets
Floor screed level 1 to 6	50%
Aluminium windows installation level 1 to 8	50%

Block A

Activity	September Targets
External Undercoat paint -rear elevation	80%
Lift electrical works and signalization	100%
Internal plaster level 6 to 7	100%
Complete power house	100%
Convenience store	100%
Boundary wall	70%
Aluminium windows installation level 1 to 4	60%



265 Elmer One

an affordable luxury

SHOWHOUSE
READY



VIPINGO DEVELOPMENT PLC



Take a sneak peek into the latest construction updates on your new home! We are excited to share the progress & milestones as your property comes to life.

Watch as each detail comes together, bringing you closer to the day you can step into your completed home. For more detailed updates or any specific inquiries, feel free to contact Centum Real Estate's offices using the information provided below:

+254 747 01 99 78
info@vipingodevelopment.com

We are here to keep you informed every step of the way.

VIPINGO CBD



Vipingo CBD is steadily transforming into a vibrant, well-connected urban destination, with roads, utilities and supporting infrastructure taking shape to create a modern commercial and mixed-use hub.



RIVIERA TOWNHOUSES

Welcome to the recent updates for Riviera Townhouses. This report provides a comprehensive overview of the progress made on-site during the past month.



Construction works are currently at the foundation stage, with extensive excavation and trenching underway across the site.

The foundation trenches have been clearly established, and excavation has progressed to the required formation levels in several sections.



August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Activity	August Targets	Progress Achieved
Design & Costing	100%	100%
Contract Award & Negotiations	100%	60%
Site Clearance court 1	100%	70%
Site hoarding	100%	60%
Foundation Excavation Court 1	80%	56%

September Targets

Looking ahead to September, our focus shifts to completing outstanding tasks from August and initiating the next activities for the project.

The following table outlines our key activities and targets for the upcoming month.

Activity	September Targets
Contract Negotiations & Award	100%
Site Clearance	100%
Site hoarding	100%
Foundation Works Court 1	40%
Foundation Works Court 2	30%



Awali Estate Phase 2

Welcome to the recent update for Awali Estate Phase 2. This report provides a comprehensive overview of the progress made on-site during the past month.

August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Activity	August Targets	Progress Achieved
Courtyard 2 - Strip footing	100%	100%
Courtyard 2 - Foundation walling	40%	50%
Courtyard 2 - Ground beam concrete works	80%	40%
Courtyard 1 - strip footing	100%	100%
Courtyard 1 - Foundation Walling	30%	40%
Courtyard 4 - Foundation excavation	70%	35%
Courtyard 4 - strip footing concrete works	75%	25%
Courtyard 5 - Foundation excavations	25%	25%
Courtyard 5 - Foundation blinding & strip footings	50%	25%
Coutyard 3 - Foundation Excavations		30%





Excavation and strip footing works have been completed in some of the houses, followed by the installation of steel reinforcement for the ground beams and completion of foundation walling.

These milestones mark solid progress in establishing a strong foundation for the townhouses.



September Targets

Looking ahead to September, our focus shifts to completing outstanding tasks from August and initiating the next activities for the project.

The following table outlines our key activities and targets for the upcoming month.

Activity	September Targets
Courtyard 2 - Foundation walling	100%
Courtyard 2 - Ground beam concrete works	100%
Courtyard 1 - Foundation Walling	100%
Courtyard 4 - Foundation excavation	100%
Courtyard 4 - strip footing concrete works	75%
Courtyard 5 - Foundation excavations	75%
Courtyard 5 - Foundation blinding & strip footings	100%
Coutyard 3 - Foundation Excavations	100%
Coutryard 3 - Foundation blinding & strip footing	100



1 & 2 Bed Block



1255 PALM RIDGE PHASE 2

Welcome to the recent update for 1255 PalmRidge Phase 2. This report provides a comprehensive overview of the progress made on-site during the past month.

August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Activity	August Targets	Progress Achieved
Block F (1 & 2 bedroom) - Foundation Excavation	100%	100%
Block H (deluxe studios) - Foundation Excavation	100%	100%
Block E (1 & 2 bedrooms) - Foundation Excavation	100%	100%
Block E (3 bedrooms) - Foundation Excavation	30%	80%
Block G - Foundations structure works	40%	70%



Following the recent groundbreaking of 1255 palmRidge phase II, significant progress has been achieved on site.

Excavation has been completed and ready to lay in foundation for the project.



September Targets

Looking ahead to September, our focus shifts to completing outstanding tasks from August and initiating the next activities for the project.

The following table outlines our key activities and targets for the upcoming month.

Activity	September Targets
Design & Costing	100%
Contract Award & Negotiation	100%
Block G - Foundation Structure works	30%
Block F - Foundation structure works	20%



KingsWood

P A R K



Welcome to the August update for Kingswood Park Retail, Gold and Platinum. This report provides a comprehensive overview of the progress made during the past month.

August Activities & Progress Achieved

The past month saw substantial progress across various construction fronts.

Below is a detailed breakdown of our August targets and the progress achieved for each key activity.

Kingswood Phase 1

Activity	August Targets	Achieved
KPLC Power Application to active Construction Sites	100%	98%
Court 8, 9, and 10 Landscaping Works(maintenance and tree planting)	100%	100%
Courts 4-11 weeding and grassing	100%	100%
Solar street lighting	30%	45%
Estate Signage	30%	50%
Common Amenities Area Design Works	60%	100%

Kingswood Phase 2

Activity	August Targets	Achieved
Sewer Reticulation Network	100%	98%
Potable and Water Reticulation Network	100%	98%
Landscaping Works(Courts and roads tree planting)	100%	98%
Other Plots Land Clearance and Vegetation Control	100%	98%
Electrical Reticulation Works	20%	30%
Ballast chips spreading on Roads in Courts 16-19	100%	70%
Cabro installation on Roads in Courts 12-15	100%	80%
Tree Planting along the feeder roads	30%	30%
Courts 12-23 Road Channels and Storm Drainage	100%	98%

Kingswood Phase 3

Activity	August Targets	Achieved
Potable and Water Reticulation Network Installation	50%	10%
Sewer Reticulation Network Installation	30%	40%
Electrical Reticulation Design and Contract Award	100%	100%
Road Base and Subgrade Construction	40%	70%
Landscaping Works(Green Courts Establishment and Levelling)	50%	80%

Kingswood Gold

Activity	August Targets	Achieved
Murram works on the Main Road	100%	50%
Subgrade works on arterial roads	10%	20%
Civil Works Design Works	100%	100%
Potable and Water Reticulation Network Design	100%	20%
Gate and Guard House Designs and Construction	50%	80%
Sample Plot Fencing and Landscaping	100%	90%

Kingswood Platinum

Activity	August Targets	Achieved
Parcel clearance works and carting debris	100%	100%
Subgrade Installation on the Main Road (Murram)	100%	10%
Civil Works Design Works	100%	50%
Potable and Water Reticulation Network Design	100%	100%
Gate and Guard House Designs and Construction	10%	10%
Sample Plot Fencing and Landscaping	100%	90%

KINGSWOOD GOLD



The gatehouse is already under construction, while road construction is also well underway, marking important milestones in the development of the project.

These works bring us closer to delivering a well-planned and welcoming community, with the overall development steadily taking shape.



September Targets

Looking ahead to the next month, our focus shifts to completing outstanding tasks and initiating the next activities for the project.

The following table outlines our key activities and targets for the upcoming month.

Kingswood Phase 1

Activity	September Targets
KPLC Power Application to active Construction Sites	100%
General Maintenance and planting of tress	100%
Courts 4-11 weeding and grassing	100%
Solar street lighting	50%
Estate Signage	50%
Common Amenities Area Design Works	100%

Kingswood Phase 2

Activity	September Targets
Sewer Reticulation Network	100%
Potable and Water Reticulation Network	100%
Electrical Reticulation Works	90%
Courts 12-23 Road Channels and Storm Drainage	100%
Ballast chips spreading on Roads in Courts 16-19	80%
Cabro installation on Roads in Courts 12-15	100%
Cabro installation on Roads in Courts 16-23	40%
Tree Planting along the feeder roads	70%
Other Plots Land Clearance and Vegetation Control	100%
Landscaping Works(Courts and roads tree planting)	100%

Kingswood Phase 3

Activity	September Targets
Potable and Water Reticulation Network Installation	20%
Sewer Reticulation Network Installation	40%
Electrical Reticulation Network Installation	10%
Road Base and Subgrade Construction	80%
Landscaping Works(Green Courts Establishment and Levelling)	90%

Kingswood Gold

Activity	September Targets
Subgrade stabilisation on the Main Road (Murram)	60%
Subgrade works on arterial roads	50%
Civil Works Design Works	100%
Potable and Water Reticulation Network Contract Award	20%
Gate and Guard House Construction	10%
Sample Plot Fencing and Landscaping	100%
Estate Boundary Tree Planting	50%

Kingswood Platinum

Activity	September Targets
Subgrade Installation on the Main Road (Murram)	30%
Civil Works Design Works	60%
Potable and Water Reticulation Network Contract Award	80%
Gate and Guard House Construction	30%
Subgrade works on arterial roads	10%
Sample Plot Fencing and Landscaping	100%
Estate Boundary Tree Planting	30%



NAIROBI



ACEK 5TH ANNUAL CONFERENCE, AT SAWELA LODGE NAIVASHA



KARURA CHAPEL RUN, AT TWO RIVERS





CONGOLESE CHAMBER OF COMMERCE DINNER, AT HOLIDAY INN TWO RIVERS



PICKLE BALL TOURNAMENT, AT TWO RIVERS

OTHER EVENTS INCLUDE:

- SIGONA GOLF CLUB TOURNAMENT
- LIMURU GOLF CLUB TOURNAMENT
- THE 5TH KENYA AFFORDABLE HOUSING CONFERENCE (KAHC) FOR KMRC, AT NAIVASHA

VIPINGO



KSPRAS CONFERENCE



CATHEDRAL MALL ACTIVATION, KAKAMEGA

The event provided a valuable platform to engage with diverse groups, build meaningful partnerships and strengthen our business network. Through these interactions, we were able to identify new opportunities for collaboration while generating potential leads that can contribute to future business growth and expansion.



Follow us on:

-  CentumRe / VipingoPLC
-  Centum Real Estate / Vipingo Development PLC
-  Centum_re / Vipingodevelopmentplc
-  Centumrealestate / Vipingodevelopmentplc



SCAN TO CREATE
TANGIBLE WEALTH

9TH FLOOR, SOUTHERN TOWER, TWO RIVERS
P.O. BOX 10518-00100 NAIROBI, KENYA

1ST FLOOR VIPINGO MARKET & BEYOND,
ALONG MOMBASA - MALINDI HIGHWAY

Nairobi Office

+254 747 01 99 77
sales@tworivers.co.ke
www.centumre.co.ke

Vipingo Office

+254 747 01 99 78
info@vipingodevelopment.com
www.vipingodevelopment.com

Entebbe Office

+256 707 76 40 20
sales@pearlmarina.co.ug
www.pearlmarina.co.ug
