

March 2026

CENTUM^{re}

Newsletter

Nairobi Office

+254 747 01 99 77
sales@tworivers.co.ke

Vipingo Office

+254 747 01 99 78
info@vipingodevelopment.com

Entebbe Office

+256 707 76 40 20
sales@pearlmarina.co.ug



SCAN TO CREATE
TANGIBLE WEALTH

Table of Contents



03

LETTER FROM THE MD

A personal note from our Managing Director

05

MONTHLY BLOG

Live, Work, Play, Shop: Reshaping Cities Post-COVID Through Mixed-Use Developments for Sustainable Growth

07

NAIROBI PROJECT UPDATES

Stay informed on the progress, milestones, and future plans for our Nairobi-based projects.

33

VIPINGO PROJECT UPDATES

Progress, milestones, and future plans for our Vipingo-based projects.



From the Managing Director

Dear Esteemed Clients,

We hope this message finds you well.

We are pleased to begin April, the month of renewal, growth and new opportunities, on a high note through the successful completion of the first phase of the Cascadia Apartments at Two Rivers.

This milestone was recently celebrated with a special occasion, providing us the opportunity to showcase the homes, appreciate their thoughtful design, and experience them firsthand as we prepare for handover to you.

Cascadia is set within the most pristine and lush section of Two Rivers Social City, and we cannot wait for you to enjoy its natural surroundings, from the confluence of the rivers and the verdant greenery to the guided promenades leading to your welcoming homes.

As we finalize the completion of the second phase, we are thrilled to invite all clients in Blocks D and E to collect their keys, and begin enjoying both the premier lifestyle and the rewarding investment benefits that Cascadia offers

Cascadia's resilient journey is a testament to our commitment to you, as well as our dedication to ensuring that you realize the full potential of your investment and lifestyle aspirations. In the same spirit, we are making strong progress across our other projects and look forward to sharing the exciting news of their completion in the coming months. Our focus remains on ensuring that every detail reflects the quality, thoughtfulness, and long-term value that define our developments.

As part of our continued commitment to supporting your investment journey, we are pleased to offer a 1.5% discount, as part of our 2026 Easter Bonanza gift. We also offer tailored mortgage solutions from leading banks, designed to help you unlock value and optimize your ownership journey through low monthly installments that are within reach. We invite you to explore these opportunities, should you, your friends, or your relatives wish to expand your investment portfolios.

Centum RE wishes you a month of renewal, great heights, and success.

Thank you for your continued trust and partnership

A handwritten signature in black ink, reading "Kenneth Mbae". The signature is fluid and cursive, with the first letter 'K' being large and stylized.

KENNETH MBAE
CENTUM REAL ESTATE



VIPINGO
DEVELOPMENT
PLC
A member of Centum Group

CENTUM^{re}



EASTER BONANZA



YOUR EASTER BONANZA BENEFITS

1.5% Off the Purchase Price – Enjoy instant savings on your dream home.

1% Furniture Contribution – Let us help you bring your space to life with a furniture boost.

Hurry! Offer Valid Until **30th April 2026!** Don't miss this limited-time opportunity to secure your home and make it truly yours. Ts & Cs Apply.



+254-747-019-978



info@vipingodevelopment.com



vipingodevelopment.com



Live, Work, Play, Shop: Reshaping Cities Post-COVID Through Mixed-Use Developments for Sustainable Growth

BY ERICK OCHIENG

The COVID-19 pandemic was more than a health crisis; it was a stress test for our cities and communities. It redefined how our cities are planned, financed and lived in. Lockdowns, disruptions of global supply chains and work from home, exposed the shortcomings of single use developments: limited access to essential services and recreation, poor integration of amenities and minimal social interaction within safe, walkable environments.

Yet, while many developments struggled to adapt, Centum Real Estate, backed by its parent, Centum Investment PLC – proved resilient. This resilience was not by chance. It was the result of a deliberate, long-term strategy conceived many years earlier to develop integrated mixed-use developments (MUDs) designed to create self-sufficient urban ecosystems.

Today, as cities rethink how we live, work and play post COVID, Centum Real Estate's vision has not only been validated – it has set up a gold standard for future-proof urban design in Kenya and Uganda.

A Strategy ahead of its Time

Long before “live – work – play” became a household phrase in the post-COVID world, CentumRE had identified the truth about future African cities: Sustainable urban development would only be possible if economic activity, housing, infrastructure, and social amenities were designed and integrated together.

Based on extensive studies, the CentumRE’s projects were not conceived as real estate developments with housing in isolation, but as economic engines – places where people can work, access essential services in minutes, entertain themselves, and benefit from shared infrastructure that is scalable. When COVID hit, this model proved adaptable, residents within our developments experienced reduced reliance on long commutes, continued access to food, retail, healthcare and open spaces and economic continuity driven by onsite commercial and service activities.

The post COVID era has reshaped priorities, and this ability to absorb shocks is one of the strongest arguments for mixed-use developments (MUDs) and CentumRE’s projects stand as proof of concept in Kenya. The prominent examples include the 106-acre Two Rivers Social City, and the upcoming 10,254-acre Vipingo Model City in Kilifi-Coast, each offering a blend of green spaces, apartments, offices, malls, special economic zones for service industries, manufacturing and logistics.

Technology, Sustainability, and Urban Resilience

While urban design continues to evolve, CentumRE uses its developments as testing grounds for the next – generation urban technologies. For example, the Two Rivers Water and Sanitation Company advanced water treatment and recycling systems with installed capacity of 2,000 cubic metres per day significantly reduce reliance on municipal supply while supporting landscaping, commercial and long-term residential use.

The same concept is adopted in Vipingo, where the 3-million litre desalination plant addresses the acute freshwater shortage in the coast, ensuring reliable supply for residents, industries and agriculture. These “technology icebreakers” positions CentumRE not only as a developer, but also as a solutions architect for Africa’s urban future.


Infrastructure That Makes Economic Sense

Across its MUDs, CentumRE has demonstrated that it makes economic sense to invest heavily in high-quality infrastructure when it serves multiple developments simultaneously. CentumRE delivers centralised road networks, power, water, and sewer systems, digital and fibre infrastructure. These investments are justified because they serve residential, commercial, industrial, and retail components. Additionally, they lower per-unit infrastructure costs, improve service reliability and long-term sustainability. This is infrastructure planned at city scale, not project scale.

From Affordable to Luxury Assets

CentumRE’s mixed use projects are built to accommodate all investors at various stages of life and lifestyle needs. The portfolio spans affordable units (2.5M-10.5M), mid-market apartments (10.5M-25M), high end residences (25M-55M), Shell-and-core options (providing flexibility for investors and occupiers to customise spaces to their lifestyle requirements), Commercial, retail, and industrial investments.

All these asset classes are supported by CentumRE’s inhouse property management team, ensuring professional estate operations, consistent service standards, long-term asset preservation and hassle free ownership for both residents and institutional investors.

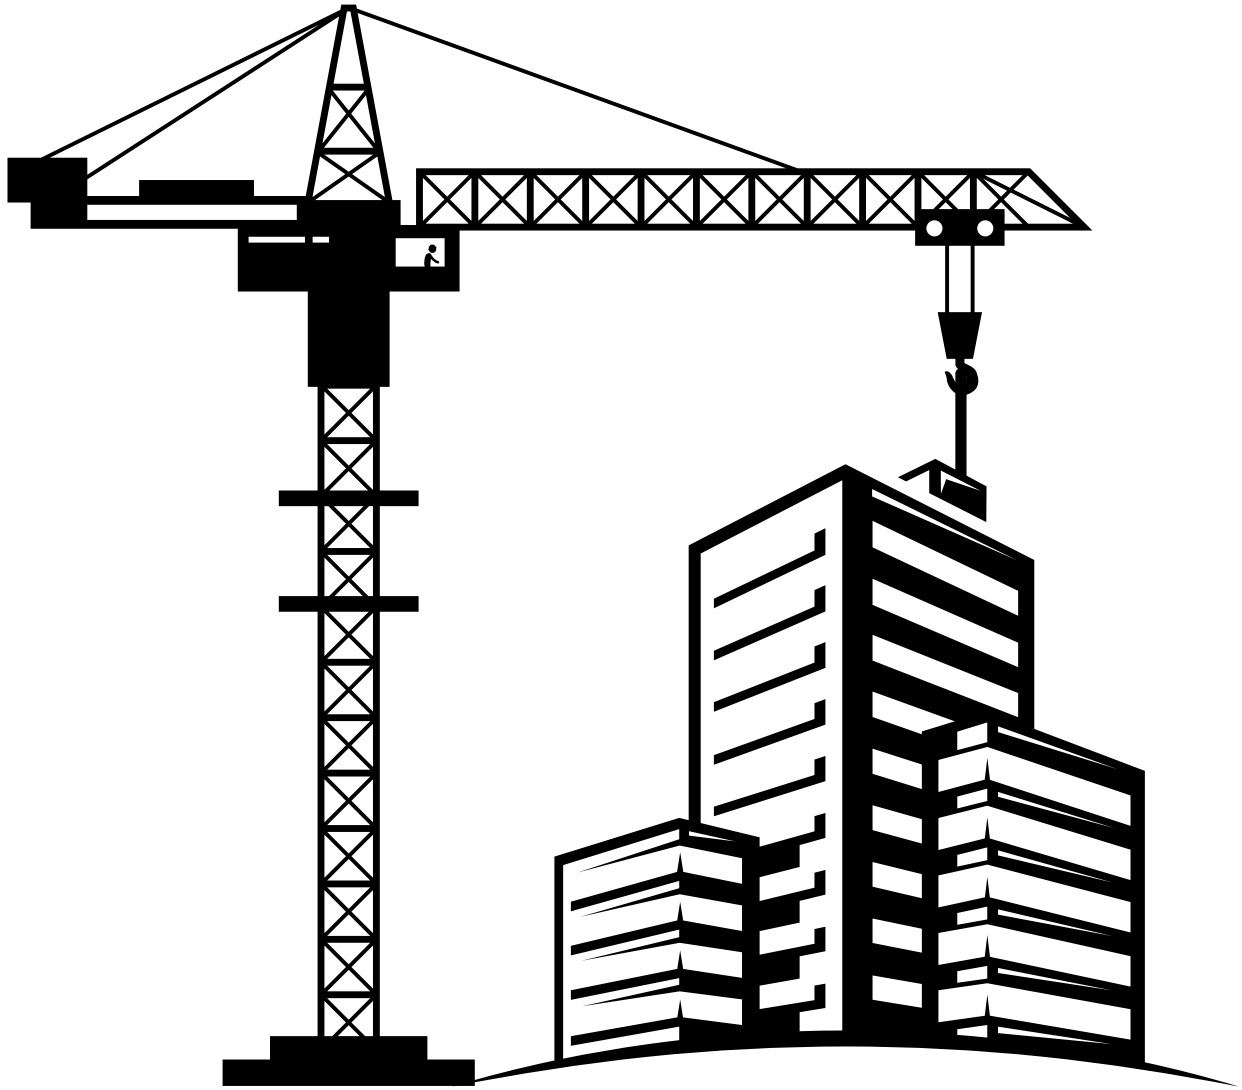

Construction Updates; Nairobi Projects

Take a sneak peek into the latest construction updates on your new home! We are excited to share the progress & milestones as your property comes to life. Watch as each detail comes together, bringing you closer to the day you can step into your completed home. For more detailed updates or any specific inquiries, feel free to contact Centum Real Estate's offices using the information provided below:

+254 747 01 99 77
centum.re@centum.co.ke

We are here to keep you informed every step of the way.

March 2026



Cascadia Apartments

MAR UPDATE

Welcome to the March update for Cascadia Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.



 Cascadia Apartments, Two Rivers

It's Time to Get Your Keys

We are excited to announce the official commencement of handovers for Cascadia Apartments Phase 1, starting **20th April 2026**.

Get in touch with our team to schedule and begin your handover journey.

Ready to see your home? Call us today!



+254 709 902 342



sales@tworivers.co.ke



centumre.co.ke

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Block D

Activity	March Targets	Progress Achieved
Lifts Installation	100%	100%
River facade sky garden balustrading	100%	100%
Level 1 to 14 corridor electrical wiring	100%	100%
Level 10 to 14 kitchen granite counter top	100%	100%
Level 1 to 14 Joinery works installation	100%	100%
Cascade D wall tiling	100%	100%
Cascade D Joinery works installation	100%	100%
Cascade D timber door leafs and locks	100%	100%
Sanitary fittings installation	100%	100%
Main Staircase balustrading level 1 to 14	100%	100%
Common area tiling	100%	100%

March Activities: Targets vs Progress

Block E

Activity	March Targets	Progress Achieved
Lifts Installation	100%	100%
River facade sky garden balustrading	100%	100%
Level 1 to 14 corridor electrical wiring	100%	100%
Level 10 to 14 kitchen granite counter top	100%	100%
Level 1 to 14 Joinery works installation	100%	100%
Cascade E floor tiling	100%	100%
Cascade E Joinery works installation	100%	100%
Cascade E timber door leafs and locks	100%	100%
Sanitary fittings installation	100%	100%
Main Staircase balustrading level 1 to 14	100%	100%
Common area tiling	100%	100%

External Works	Mar Targets	Progress Achieved
Boundary wall along Limuru road- walling plasterworks	100%	100%
Boundary wall along Limuru road- Electric fence installation	50%	90%
Landscaping works along Limuru road	100%	80%

Mar Activities: Targets vs Progress

Other Blocks status in Cascadia Apartments


Block A	Progress
Sub structures	100%
Super Structures (level 1 to level 14 slabs done)	100%
Superstructures level 15 slab- Roof slab	100%
External Masonry works	80%
Internal Masonry works	70%
Electrical first fix	30%
Plumbing first fix	30%
Block B	Progress
Sub structures	100%
Super Structure	100%
External Masonry works	100%
Internal Masonry works	100%
External plasterworks -River facade	100%
External plasterworks-Two rivers facade	100%
Internal floor screed	90%
Internal door frames	70%
Internal wall skimming	32%
External aluminium window frames	32%

Mar Activities: Targets vs Progress

Block C

Block C	Progress
Sub structures	100%
level 1 to level 7 slabs done	100%
Level 8 slab works	80%
Cascade floors level -3 slab	100%
Cascade floors level -2 slab	100%
Cascade floors level -1 slab	100%
Cascade floors level 0 slab	100%

Photos of Mar Construction Progress

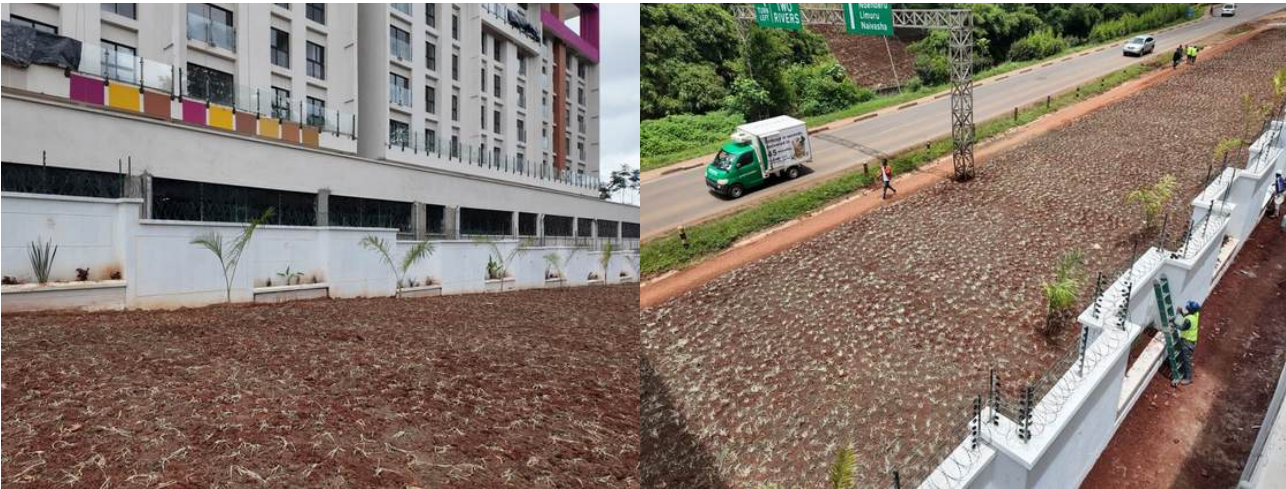

Landscaping along Limuru road





Basement 1 Parking



Block C Level 7



Block B Corridor

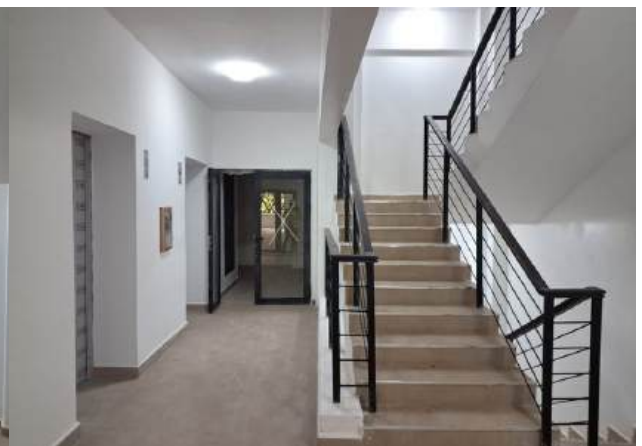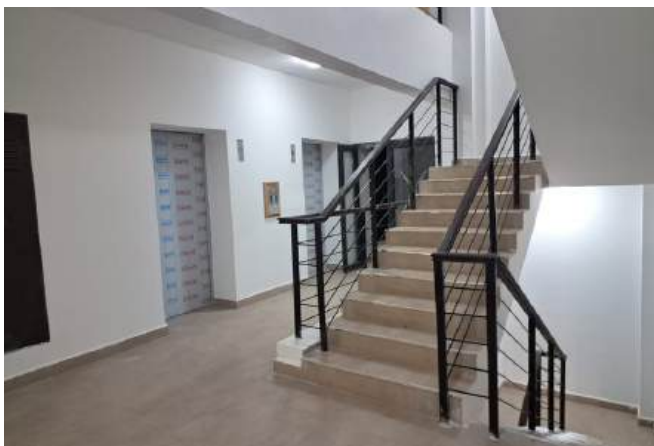

Block B Staircase



Boiler Installation



Sanitary Works




Kitchen Fixtures



Block D & E



Curtain Walling

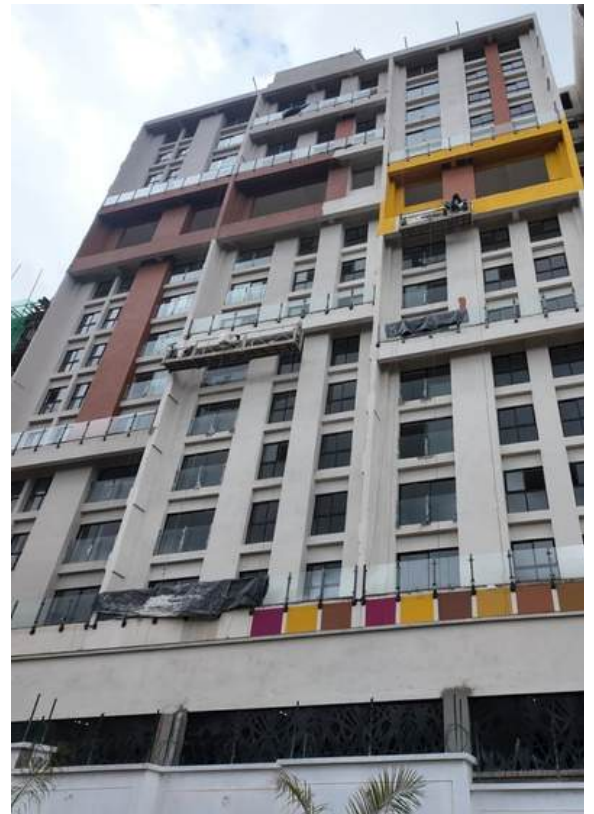

April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for the Cascadia Apartments project. The following table outlines our key activities and targets for the upcoming month.

Block D and E

Activity	April Targets
Snagging Units	100%
Snagging Common areas	100%
Testing and commissioning Lifts	100%
Testing and commissioning Plumbing systems	100%
Testing and commissioning Electrical systems	100%
Installation, testing & commissioning of Kitchen Appliances	100%
Installation, testing & commissioning ICT Systems	100%

External Works	April Targets
Boundary wall along Limuru road- Electric fence installation	100%
Boundary wall along Limuru road- Painting	100%
Landscaping works along Limuru road	100%

March 2026



265 Elmer One

Mar Update

Welcome to the March update for 265 Elmer One Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Activity	March Targets	Progress Achieved
Block C;		
Internal plaster	100%	98%
Complete roofing works (structure & covering)	100%	70%
Complete lift installation & commissioning	100%	40%
Staircase railing	50%	10%
External Undercoat paint	100%	70%
Complete MEP first fixes level 8	100%	100%
Floor screed level 1,2,3	100%	30%
Aluminium windows installation level 1 to 4	100%	35%
Block B		
Internal plaster level 5,6 & 7	100%	100%
MEP First fixes level 2 to 7	100%	100%
Preparation for screed works level 1,2,3	100%	100%

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Activity	March Targets	Progress Achieved
Block A		
External plaster – rear face	100%	50%
Lift rails installation	100%	20%
Complete roofing works	100%	70%
MEP First fixes level 2 to 5	100%	100%
External works/structures		
Complete power house	100%	40%
Convenience store	100%	10%

April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for 265 Elmer One Apartments. The following table outlines our key activities and targets for the upcoming month.

Activity	April Targets
Block C;	
Complete roof covering	100%
Complete lift installation & commissioning	100%
Staircase railing	50%
External Undercoat paint	100%
Floor screed level 1,2,3,4	100%
Aluminium windows installation level 3 to 8	100%
Block B	
Preparation for screed works level 3 to 7	100%
Floor screed level 1 to 3	100%
External Undercoat paint	60%
Block A	
External plaster – rear face	100%
Lift rails installation	100%
Complete roofing works	100%
MEP First fixes level 5 to 8	100%
Internal plaster level 1 to 2	100%
Complete power house	100%
Convenience store	100%
Boundary wall	60%

External works/structures	April Targets
Complete power house	100%
Convenience store	100%

Photos of March Construction Progress



Plastering Works

Photos of March Construction Progress



Roofing works




Block C Undercoat



Internal Plastering

**SHOWHOUSE
READY**

265 Elmer One

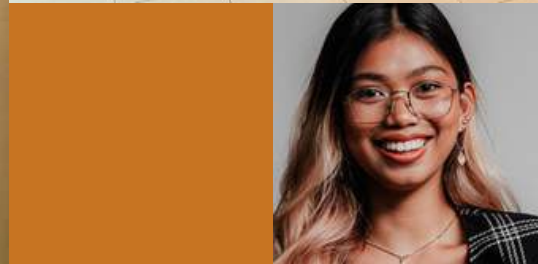

265 Elmer One
an affordable luxury

March 2026



26 Mzizi Court

Mar UPDATE

Welcome to the March update for 26 Mzizi Court Apartments. This report provides a comprehensive overview of the progress made on-site during the past month.

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Block C

Activity	March Targets	Progress Achieved
External plasterworks – Courtyard façade.	100%	100%
External plasterworks – Rear façade.	100%	100%
Internal plaster at level 6 to 10.	100%	80%
Level 18 columns, shear walls & lift shaft concreting.	60%	100%
Walling at level 14 to 17.	100%	70%

Block B

Activity	Mar Targets	Progress Achieved
Internal plasterworks level 13 to 16.	100%	95%
External aluminium windows – Office façade.	75%	50%
Lift center beam level 11 – 18 lower roof concreting.	100%	100%
Floor screeding at level 8 to 11.	50%	90%

Photos of March Construction Progress



Block B Lift center beam & parapet wall coping works



Block C Internal Plaster at level 8

Photos of March Construction Progress



Block B Internal Plaster



Block B Skimming and installation of door frames at level 8



Photos of March Construction Progress



Block B and C



Mzizi Phase 2 – Excavation work ongoing

April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for the 26 Mzizi Court Apartments project. The following table outlines our key activities and targets for the upcoming month.

Block C

Activity	April Targets
Internal plaster at level 6 to 10.	100%
Walling at level 14 to 17.	100%
Parapet wall coping formwork & concreting.	100%
Aluminium window frames installation	50%
Internal plaster at level 6 to 10.	100%

Block B

Activity	April Targets
Internal plasterworks level 2- 17	100%
External aluminium windows – All façades	100%
Floor screeding at level 2-17	100%
Internal skimming at level 2-17	100%
Installation of door frames at level 2- 17	100%
Joinery works fabrication offsite	100%
External undercoat painting- All facades	100%



NEW
26 MZIZI COURT
ShowHouse

+254 747 01 99 77
sales@tworivers.co.ke

Lakeside Living

In Timeless Comfort



Riviera Residencies

Welcome to Riviera Residencies, where thoughtful design meets tranquil living on the shores of Lake Victoria. Located within the master-planned Pearl Marina Estates in Garuga, Entebbe, these elegant 3 bedroom townhouses offer more than a home they offer a lifestyle surrounded by nature, serenity, and security.

With 22 units built in phase I, Riviera Residencies combines modern architecture with family functionality. Each home is crafted to offer seamless indoor-outdoor flow, blending comfort with timeless finishes. Security, privacy, and accessibility are all part of the plan.

Featuring

- 3 Bedrooms + Ensuite DSO
- 2 Living Rooms
- Dining Area
- 2 + 1/2 Bathrooms
- Open-Plan Kitchen
- Private Yard & Parking
- Gated Community

80%

Construction Complete



Part of Something Bigger: Pearl Marina Estates.

Nestled within Pearl Marina's 389-acre lakeside estate, a vibrant community of villas, bungalows, apartments, serviced plots, and shared amenities like green parks, a beach zone, and nature trails. This is a destination for those who value legacy, location, and lakeside living.



Come see it for yourself



+256 764 531 050, sales@pearlmarina.co.ug, Garuga, Entebbe



Construction Updates ; Vipingo Projects

Welcome to the Construction Updates section for Phase 2 of our Vipingo development! We are excited to announce that Phase 2 has officially commenced, and we will be sharing regular updates on the progress right here. Stay tuned to see how your future home is taking shape. If you would like a more detailed update or have any questions, feel free to contact Vipingo Development's offices directly at:

+254 747 01 99 78

info@vipingodevelopment.com

March 2026



Awali Estate Phase 2

Mar UPDATE

Welcome to the March update for Awali Phase 2. This report provides a comprehensive overview of the progress made on-site during the past month.

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Phase 2 Rollout

March

Activity	Target	Achieved
Cluster 1-5		
Site Preliminaries (Site Office, Hoarding)	100%	100%
Foundation Excavation (Court 01)	100%	85%
Concrete Blinding (Court 01)	100%	85%
Foundation Excavation (Court 02)	80%	60%
Concrete Blinding (Court 02)	40%	15%
Roads Opening and cart away (Courts 01 and 02)	30%	20%
External Services Works (Courts 01 and 02)	10%	0%

Renders



April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for the Awali Estates project. The following table outlines our key activities and targets for the upcoming month.

Activity	Target
Cluster 1-5	
Foundation Excavation (Courts 1 and 2)	100%
Concrete Blinding (Courts 1 and 2)	100%
Strip Footing and Foundation Walling (Courts 01 and 02)	100%
Backfilling and compacting (Courts 01 and 02)	30%
Ground Floor Slab Casting (Court 01 and 02)	30%
Roads Opening and cart away (Courts 01 and 02)	30%
External Services Works (Courts 01 and 02)	10%

Renders



Phase 2 Rollout

March Progress Photos



March 2026

1 & 2 Bed Block



1255 PALM RIDGE PHASE 2

Mar UPDATE

Welcome to the March update for 1255 PalmRidge Phase 2. This report provides a comprehensive overview of the progress made on-site during the past month.

March Activities: Targets vs Progress

The past month saw substantial progress across various construction fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Activity	Target	Achieved
Cluster 1		
Design Optimization	100%	100%
Costing and Contract Award	60%	20%
Site Clearance	100%	20%
Site Preliminaries (Site Office, Hoarding)	50%	0%
Foundation Excavation	20%	0%



Site Cleared


April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for 1255 Palm Ridge. The following table outlines our key activities and targets for the upcoming month.

Activity	Target
Cluster 1	
Costing and Contract Award	100%
Site Clearance	100%
Site Preliminaries (Site Office, Hoarding)	100%
Foundation Excavation	20%



March 2026

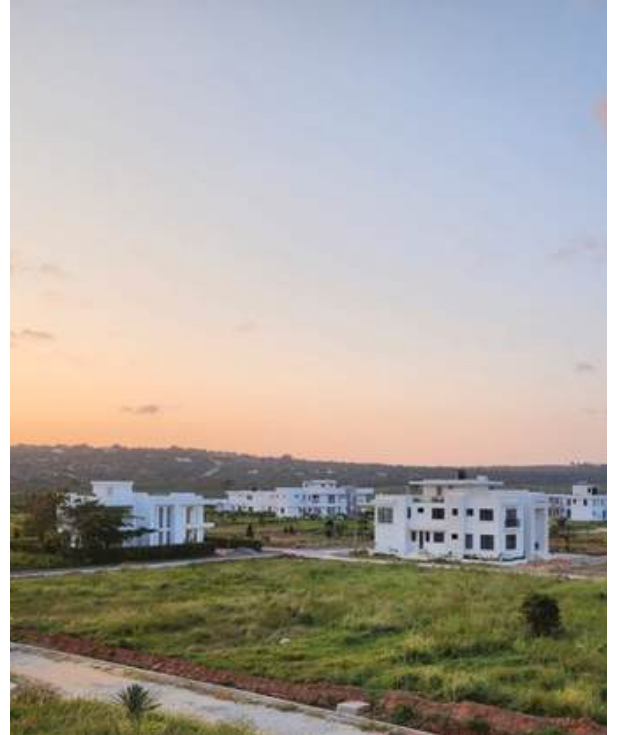

KINGSWOOD SERIES

Welcome to the March update for Kingswood Park Retail, Gold and Platinum. This report provides a comprehensive overview of the progress made during the past month.



Mar UPDATE

Kingswood HomeOwners Progress



Kingswood Park Gold and Platinum



Gatehouse Construction

Other progress updates in Vipingo



Renders of Fuel station in Vipingo



Fuel station under construction in Vipingo



Renders and progress photo of a school under construction in Vipingo



Desalination Boundary Wall Construction



Desalination Boundary Wall Construction

March Activities: Targets vs Progress

The past month saw substantial progress across various fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Kingswood Phase 1

Activity	Target	Achieved
KPLC Power Application to active Construction Sites	100%	90%
Court 6,7,8, and 9 Landscaping Works(maintenance and tree planting)	100%	100%
Courts 4-11 weeding and grassing	100%	100%
Solar street lighting	30%	20%
Estate Signage	50%	20%
Common Amenities Area Design Works	20%	10%

Kingswood Phase 2

Activity	Target	Achieved
Sewer Reticulation Network	100%	90%
Potable and Water Reticulation Network	100%	95%
Landscaping Works(Courts and roads tree planting)	100%	95%
Other Plots Land Clearance and Vegetation Control	100%	90%
Electrical Reticulation Works	30%	20%
Ballast chips spreading on Roads in Courts 16-19	100%	70%
Cabro installation on Roads in Courts 12-15	100%	80%
Tree Planting along the feeder roads	30%	30%
Courts 12-23 Road Channels and Storm Drainage	100%	70%

Kingswood Phase 3

Activity	Target	Achieved
Potable and Water Reticulation Network Installation	50%	20%
Sewer Reticulation Network Installation	30%	20%
Electrical Reticulation Design and Contract Award	100%	100%
Road Base and Subgrade Construction	40%	20%
Landscaping Works(Green Courts Establishment and Levelling)	50%	25%

April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for Kingswood Park. The following table outlines our key activities and targets for the upcoming month.

Kingswood Phase 1

Activity	Target
KPLC Power Application to active Construction Sites	100%
Courts 4-11 weeding and grassing	100%
Solar street lighting	50%
Estate Signage	50%
Common Amenities Area Design Works	100%

Kingswood Phase 2

Activity	Target
Sewer Reticulation Network	100%
Potable and Water Reticulation Network	100%
Electrical Reticulation Works	50%
Courts 12-23 Road Channels and Storm Drainage	100%
Ballast chips spreading on Roads in Courts 16-19	80%
Cabro installation on Roads in Courts 12-15	100%
Cabro installation on Roads in Courts 16-23	20%
Tree Planting along the feeder roads	100%
Other Plots Land Clearance and Vegetation Control	100%
Landscaping Works(Courts and roads tree planting)	100%

Kingswood Phase 3

Activity	Target
Potable and Water Reticulation Network Installation	50%
Sewer Reticulation Network Installation	50%
Electrical Reticulation Network Installation	50%
Road Base and Subgrade Construction	40%
Landscaping Works(Green Courts Establishment and Levelling)	50%

Kingswood Gold and Platinum

The past month saw substantial progress across various fronts. Below is a detailed breakdown of our March targets and the progress achieved for each key activity.

Kingswood Gold

Activity	Target	Achieved
Murram works on the Main Road	100%	50%
Subgrade works on arterial roads	10%	5%
Civil Works Design Works	100%	50%
Potable and Water Reticulation Network Design	100%	100%
Gate and Guard House Designs and Construction	50%	25%
Sample Plot Fencing and Landscaping	100%	90%

Kingswood Platinum

Activity	Target	Achieved
Parcel clearance works and carting debris	100%	100%
Subgrade Installation on the Main Road (Murram)	100%	10%
Civil Works Design Works	100%	50%
Potable and Water Reticulation Network Design	100%	100%
Gate and Guard House Designs and Construction	10%	10%
Sample Plot Fencing and Landscaping	100%	80%

April Activities and Targets

Looking ahead to April, our focus shifts to completing outstanding tasks from March and initiating the next activities for Kingswood Park. The following table outlines our key activities and targets for the upcoming month.

Kingswood Gold

Activity	Target
Subgrade Installation on the Main Road (Murram)	100%
Civil Works Design Works	100%
Potable and Water Reticulation Network Contract Award	100%
Gate and Guard House Construction	50%
Subgrade works on arterial roads	20%
Sample Plot Fencing and Landscaping	100%
Estate Boundary Tree Planting	20%


Kingswood Platinum

Activity	Target
Subgrade Installation on the Main Road (Murram)	30%
Civil Works Design Works	100%
Potable and Water Reticulation Network Contract Award	100%
Gate and Guard House Construction	20%
Subgrade works on arterial roads	20%
Sample Plot Fencing and Landscaping	100%
Estate Boundary Tree Planting	20%

Vipingo at Glance



Vipingo Special Economic Zone

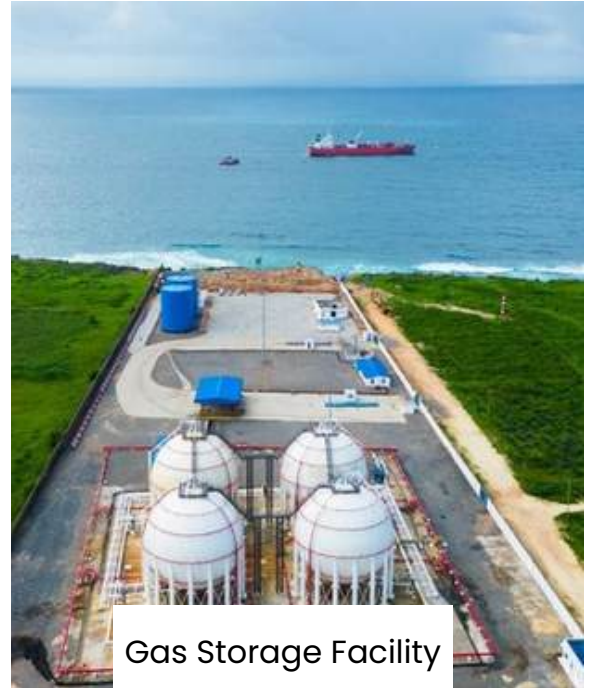

Gas Storage Facility



Cashew Nut Factory



MiniMall



Water Desalination Plant



Upcoming Petrol Station



March

EVENT GALLERY





Walk and Jog
CASCADIA EVENT



THE REAL CONVERSATION

The go-to podcast for everything Real Estate

SEASON TWO



Do you want to learn about the current real estate trends? How to invest in real estate? or how to increase your investment value? Then 'The Real Conversation' is your perfect companion. Join Mercy and Ednah every Thursday at 4pm on Youtube and Spotify for very entertaining and educative real estate insights.

Follow our social media platforms to stay up to date on the conversation

 Centum Real Estate


 @therealconversationke

 Spotify The Real Conversation Ke

 TikTok @therealconversationke



NEW EPISODES EVERY WEEK



ENVISION YOUR RETIREMENT

YOUR WAY WHILE YOU CAN

Your Best Years Deserve The Best Home & Community at Kingswood Gold

📍 VIPINGO, KILIFI

½ & 1 ACRE PLOTS

PRICE FROM | **KES 10M**



Exclusive
Gated
Community



Serviced
Plots



24/7 Fresh
Desalinated
Water



Amenities
in Place

+254 747 019 978

info@vipingodevelopment.com



9TH FLOOR, SOUTH TOWER, TWO
RIVERS P.O. BOX 10518-00100 NAIROBI,
KENYA

Nairobi Office

+254 747 01 99 77
centum.re@centum.co.ke
www.centumre.co.ke

Vipingo Office

+254 747 01 99 78
info@vipingodevelopment.com
www.vipingodevelopment.com

Entebbe Office

+256 707 76 40 20
sales@pearlmarina.co.ug
www.pearlarina.co.ug

Follow us on:

 @CentumRe / @VipingoPLC

 Centum Real Estate / Vipingo Development PLC

 centum_re / vipingodevelopmentplc

 @centumrealestate / @vipingodevelopmentplc

